
Environmental Assessment Report

Union Road (UNR)

Name of the Sub-project :Shilmandi U.P Office (South Shilmandi)-Shilmandi Natun Bazar Road

Slice No. :UNR-26 (A)

Upazila :Narsingdi Sadar

District :Narsingdi



Second Rural Transport Improvement Project
Local Government Engineering Department

Contents

1. Sub Project Description	3
2. Detail Environmental Features	5
3. Baseline Data: Physical Environment	6
4. Screening Format.....	9
5. Specific Impact and Mitigation	13
6. Environmental Management Plan	15
7. EMP in Bidding Document	20
Annex-1: Public Consultation	21

1. Sub Project Description

Name of the Sub-project : Shilmandi U.P Office (South Shilmandi)-Shilmandi Natun Bazar Road.

ID No. : 368603020

District Name : Narsingdi

Name of the Upazila : Narsingdi Sadar

Length of the Road : 4.5km (Effective 1.63 km)

Location of the sub-project

Narsingdi Sadar Upazila is located at 23.9167°N & 90.7250°E and bounded by Shibpur, Raipura, Palash, Bancharampur, Rupganj and Araihaazar Upazila as shown in location map. The road is 4.5 km (Effective length 1.63 km long, starts at Shilmandi U.P Office and ends at South Shilmandi Charsindar RHD Road [details are listed in **Table-1.1**].

Name of the unions the road passes through	Name of the road side villages (at least 5 nos)	Starting point of the road	End point of the road	Year of construction/Last maintenance	Major items included in estimates
Shilmandi	Shilmandi , Shilmandi Middle, Shilmandi South	Shilmandi U.P Office	South Shilmandi Charsindar RHD road	No Maintenance	Earth Work, WBM, ISG, Brick on End Edging, Dense Carpeting & Surface Drain



Table-1.1

Brief Description of the sub project

Union road (UNR) improvement includes construction of bituminous road on the existing earthen road. The road has a length of 4.5 km (Effective 1.63 km). At present BC road exist at chainage 0.00m to 2000m, 2700m to 2725m and 3380m to 3600m. Major components of the works include earthwork (earth volume 4178.70cums), base coarse Improve sub grade, Brick at edge, 25mm dense carpeting etc. Drainage Structure such as Box Culvert is required at chainages 2700m and 4200m.



Photograph of the proposed Road

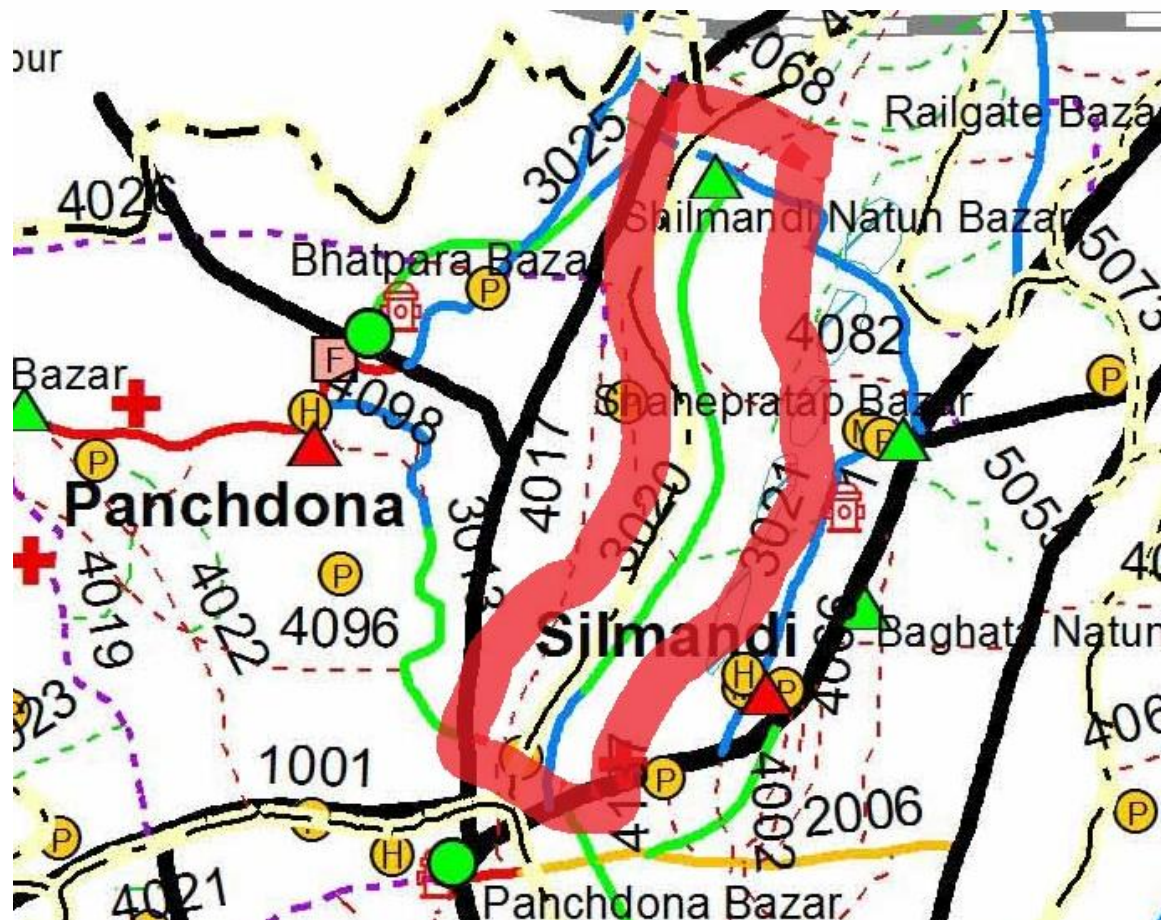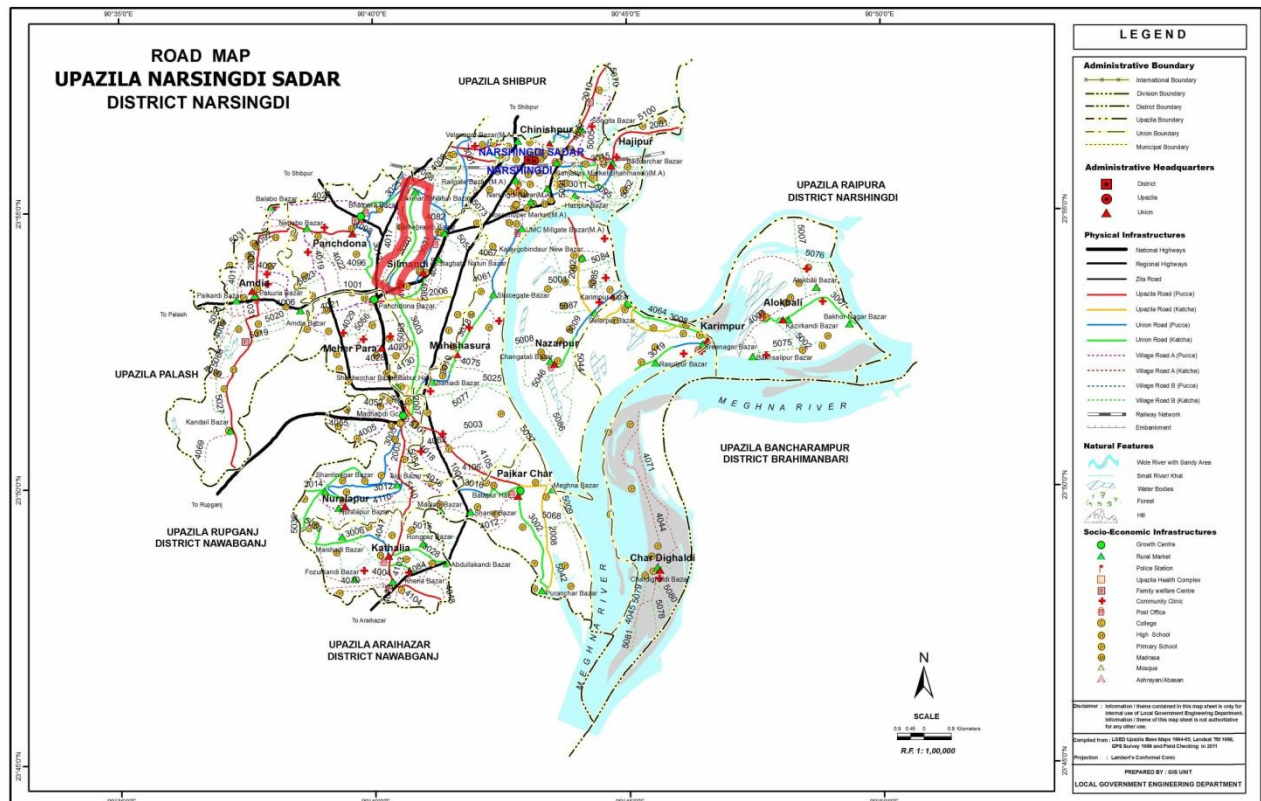

Location map of the sub project

2. Detail Environmental Features

The UNR has a length of 4.50 km (effective length 1.63 km). Detail Environmental features within 100m of the both sides from the centre line were collected @300m longitudinal intervals. The findings of the survey for the aforementioned road can be seen in the table below:

Chainages	Right	Left	Environmental Features
00-300	√		School, Shop, Community Clinic, Grameen Bank
		√	Small Industry, Housing Area
300-600	√		Small Industry, Agricultural Land
		√	Small Industry, Housing Area, Shop
600-900	√		Primary School, Club, Agricultural Land
		√	Shop, Housing Area
900-1200	√		Old Brahmaputra River, Shop, Agricultural Land
		√	Housing Area, Small Industry, Agricultural Land
1200-1500	√		Old Brahmaputra River
		√	Shop, Housing Area, Agricultural Land
1500-1800	√		Old Brahmaputra River, Agricultural Land
		√	Agricultural Land
1800-2100	√		Agricultural Land
		√	Housing Area
2100-2400	√		Housing Area
		√	Housing Area
2400-2700	√		Shop, Agricultural Land
		√	Market, Agricultural Land
2700-3000	√		Housing Area, Shop
		√	Agricultural Land
3000-3300	√		Housing Area, Shop
		√	Agricultural Land
3300-3600	√		Agricultural Land
		√	Agricultural Land
3600-3900	√		Housing Area, Agricultural Land
		√	Agricultural Land
3900-4200	√		Housing Area, Agricultural Land
		√	Agricultural Land
4200-4500	√		Housing Area, Agricultural Land, Shop
		√	Housing Area, Agricultural Land, Shop

3. Baseline Data

3 (a) Physical Environment

3. a. 1 Atmosphere and Climate

Meteorological conditions of the area are more or less similar to the central part of the country with respect to temperature, rainfall and humidity. The subproject area is situated in humid sub-tropical climate with large variations between summer and winter temperatures and significantly influenced by monsoons during the months of May to September when most of the rainfall occurs. The annual average maximum temperature is about 36⁰C and minimum temperature is about 12.7⁰C. Annual rainfall is about 1,329 mm (ref. Dhaka, 2012).

3.a.2 Topography

The sub-project area mainly comprises of plain agricultural land and almost flat with few undulations. River Old Brahmaputra flows nearby the sub-project area. The depressions and canals are dominated by organic clay and peats. Most depression and canals are tectonically controlled. The average ground elevation of the project area is about 13m PWD. According to the information collected through public consultation, this area is considered as a flood affected area and affected in severe floods of 1988, 1998 and 2004. A general topographic condition is found in the flowing photograph:



3.a.3 Drainage

Drainage congestion was observed at chainages 2700m and 4200m surrounding the road due to lack of opening to drain out water. Drainage congestion may also occur during construction of drainage structures.

3.a.4 Water Quality

3.a.4.1 Ground Water: Information on ground water quality of the nearest tube-wells along the road has been collected on spot discussion and consultation with the villagers. The depth of ground water level varies from 4m to 7m. Potable ground water is available at an average depth of 130m to 220m. Ground water quality of HTWs for drinking purposes (Narshingdi District) is provided in the following table:

Drinking water quality parameters	Average Contents of HTW water (mg/L)	Permissible limit (mg/L), Bangladesh standard	Comments
Arsenic	0.007	Up to 0.05	Within permissible limit
Iron	0.87	Upto 1.00	Exceed permissible limit
Chloride	27	150-600	Below the standard range

Source: Bangladesh Drinking Water Quality Survey, 2009 by BBS & UNICEF

3.a.4.2 Surface Water: The road sub project crosses large number of water bodies such as small and medium ponds which are used for multiple purposes. The surface water in ponds is not saline but is not suitable for drinking purposes due to pollution. All the ponds are man-made and used for fishing, water supply and domestic uses. River Old Brahmaputra flows nearby the sub-project area. Some small and medium industries observed near the subproject which are remarkable sources of water pollution.

3.a.5 Noise

Noise is not a major impediment for the quality of the environment in the study area. Vehicles such as motor cycle, tempo, mini truck, votvoti, tractor trailer etc. move on the road during day and night. These vehicles generate noise in the subproject area but within tolerable limit in most cases. Some small and medium industries observed near the subproject generate noise.

3.a.6 Air Quality

Ambient air quality data was not available. Quality of air appears to be clean but due to poor condition of road surface, dust is generated, especially during the movement of vehicles that causes air pollution. There are some small and medium industries observed near the subproject which are the sources of air pollution.

3. Base line data: (b) Biological Environment

Flora & Fauna

The project area has some flora of commercial importance. The major tree species found in the area are Mahogany, Shishu, Rain-tree and (in Bengali and colloquial) Simul, Eucalyptus, Arjun, Minjiri, Jarul, Hizal, Sheora, Debbaru, Siris, Royna, Koroï etc. No endangered floral species are reported. The dominant fruit-bearing trees include Jackfruit, Banana, Mango, Wood apple, Papaya, Lemon, Coconut, Betel nut etc.

Besides domestic animals, wild dogs, jungle cat, jackal, mongoose, Guishap (Lizard), Porcupine and rodents like ants and snakes of various species are reported, though having a decreasing trend. The amphibians include Kola bang, Kuno bang, Gekhho bang etc. are available, although to a lesser extent. The endangered animals like Wild cow, Wild Buffalo, Peafowl, Mugger

Crocodile etc. are not reported. Some birds found in common Bengali name include Chorui, Doel, Ghugu, Shalikh, Chil, Pecha, Holudpakhi, Masranga, Tia, Bok, Kak, Tuntuni, Bulbuli, Kokil, Kath thokra etc.

3(c)Stakeholder Consultation:

During the data collection, public consultation meeting were held at Shilmandi Bazar. The list of participants, photograph and details of the discussion meeting are attached as Annex-1 and their recommendations are highlighted below:

- Adequate drainage facilities to be provided at all chainages to avoid water accumulations or congestion.
- Effective measure to be taken to minimize all the adverse environmental impacts of road construction works.
- Steps to be taken for minimizing the air pollution by spraying water at the construction sites.
- Noise pollution to be effectively minimized up to a tolerable limit.

4. Screening Format

Screening format was administered for identifying the impacts and their extents and the screening data sheet for this subproject is given below:

Screening Questions	Yes	No	Scale of Impact			Remarks
			High	Medium	Low	
A.Potential Environmental Impacts during planning and design phase/ Sub-project siting. Is the sub-project area adjacent to or within any of the following environmentally sensitive areas?						
▪ Protected Area (Forest)		√				The area is not included in designated protected area.
▪ Wetland (Beel, Haor)		√				The area is not located in designated Wetland.
▪ National Park		√				The road has no encroachment of any national park.
▪ Wildlife sanctuary		√				The road is not included in any wildlife sanctuary.
▪ Buffer zone of protected areas		√				The area does not belong to buffer zone of any protected area.
▪ Special area for protecting biodiversity		√				The area does not belong to any special area for protecting biodiversity.
B.Potential Environmental Impacts from construction of new roads. Will the sub-project cause.....						
▪ Loss of agricultural land?		√				Required earth will not be collected from agricultural land.
▪ Negative effects on rare (vulnerable), threatened or endangered species of flora or their habitat?		√				No rare species of flora and fauna occur near by the sub-project area.
▪ Negative effects on designated wetlands?		√				The area is not included in any designated wetland.
▪ Negative effects on wildlife habitat, populations, corridors or movement?		√				No wildlife habitat reported to exist nearby the sub-project area.
▪ Negative effects on locally important or valued ecosystems or vegetations?	√				√	Care will be taken, so that local important or valued ecosystem or vegetation is not damaged. Turfing will be done to compensate the loss of

Screening Questions	Yes	No	Scale of Impact			Remarks
			High	Medium	Low	
						vegetation.
▪ Destruction of trees and vegetation?	√					Vegetation may be removed during construction of road. Turving will be done after the construction.
▪ Impact on fish migration and navigation?		√				The sub-project does not cross any water bodies.
▪ Obstruction of natural connection between river and wetlands inside project area?		√				The sub- project does not cause any obstruction to any natural connection between river and wetlands
▪ Water logging in areas?	√				√	Baseline data shows that water are logged at 2700m and 4200m. Water logging may also occur due to construction activities. Drainage structure and sufficient opening to drain out water at the above mentioned chainages will be provided to avoid water logging.
▪ Insufficient drainage?	√				√	From baseline date it has been observed that there is insufficient drainage at the above mentioned chainages. So, drainage structure will be provided to increase drainage facility.
▪ Negative effects on surface water quality?	√				√	No liquid / solid waste will be disposed off in water bodies
▪ Negative effects on groundwater quality, quantity or movement?		√				Liquid / solid waste will not be allowed to dispose in ground directly.
▪ Loss of existing buildings, property, economic livelihood?		√				No land acquisition or resettlement is required
▪ Increased soil erosion and/or sedimentation?	√				√	Soil may erode during earth work at slope but turving and compaction will be carried out after completion of earth work.
▪ Negative impact on soil stability and compactness?	√				√	Turving on embankment top and slope will be provided to

Screening Questions	Yes	No	Scale of Impact			Remarks
			High	Medium	Low	
						mitigate negative impact on soil stability and compactness.
▪ Impacts on sustainability of associated construction waste disposal?		√				Construction waste will be disposed in safe place.
▪ Traffic disturbances due to construction material transport and wastes?	√				√	Minimum disturbance is anticipated
▪ Increased noise due to transportation of equipment and construction materials?	√				√	Occur some disturbance within acceptable limit
▪ Increased noise due to day-to-day construction activities?	√				√	Occur some noise disturbance but within acceptable limit
▪ Increased wind-blown dust from material (e.g. fine aggregate) storage areas?	√				√	Proper environmental code of practice will be in place by spraying of water during construction to reduce dust emission.
▪ Health risks to labors involve in activities?	√				√	Some risk during construction is anticipated which will be taken care of by adopting remedial measures incorporated in the contract
C. Potential Impacts of the Improved road. Will the improved road cause						
▪ Negative effects on neighborhood or community characters?		√				No negative effect anticipated
▪ Negative effects on local business, institutions or public facilities?		√				Improved road will increase the local business
▪ Potential social conflict between occupational groups-farmers vs. fisheries?		√				The proposed subproject will not cause any conflict between occupational groups, e. g. farmers and fishermen
▪ Degradation or disturbance of historical or culturally important sites (mosque, graveyards, monuments etc.)?	√				√	There exists no historical or cultural important sites to be damaged/degraded by the proposed road., there exist mosques, where some care to be involved during construction, where

Screening Questions	Yes	No	Scale of Impact			Remarks
			High	Medium	Low	
						communication will be improved afterwards.
▪ Blockage of navigation system?		√				No navigation system will be blocked by the road. However, if such issue arises the road alignment to be diverted to avoid blockage of navigation
▪ Impediments to movements of people and animals?	√				√	No impediment to movement of people and impediment to movement of animals will be negligible since the road is not wide enough.
▪ Conflicts in water supply rights and related social conflicts?		√				Will not create any social conflict over water supply rights.
▪ Air quality?	√				√	Construction work will involve Earth work, WBM, Brick on end Edging, Carpeting and Surface drain etc. will lead to increase in dust/suspended particulate matter (SPM) around the construction site. Spraying of water; bituminous burning unit to be placed away from residential area, educational/religious institutions to reduce air pollution.

Assessment:

The proposed sub-project (Road improvement) is not located within any environmentally sensitive area and thus will not create intimidation to important environmental features. In some locations drainage congestion has been observed and drainage system will be developed to minimize the water logging of those particular locations. Some earthwork will be involved, but no agricultural productive soil will be used for the purpose. Earth will be compacted for stabilization. The inputs will be mainly at construction phase and limited within project boundary. Moreover, mitigation measures will be taken according to the EMP for minimizing the air, dust and noise pollution.

5. Specific Impact and Mitigation

This sub-project involves the improvement work of 4.5 km (Effective 1.63 km) road, which passes through different types of environmental features like pond, agricultural land, shop/ bazar, mosque, school etc. For the purpose environmental studies have been carried out (with all the details of individual environmental components) since it is apprehended that, some adverse environmental effects will take place on the existing physical environment. The possible impacts of the improvement work on this road and their mitigation measures have been discussed (component-wise) below:

5.1 Earth Work: The road improvement work consists of earth excavation, earth filling and cutting, removal of unsuitable materials or top soil, preparation of embankment layer, hard shoulder preparation, protective work, etc. These works lead to slope erosion, silt deposition on crop fields, dust blowing, noise and vibration disturbing the local people. As no massive earth work is involved at any specific location, several small volumes of earth from different areas will be arranged by the contractor. However, if large volume of earth is required, the borrow pit may be converted to deeper pond (suitable for fish cultivation).

Mitigation:

- Proper care will be taken during cutting and filling so that slope or toe of the road embankment remain within the right of way and does not disturb the crop.
- Turfing & compaction will be done on the shoulder and slope.

5.2 Temporary interruption of natural drainage and local drainage congestion: Drainage congestion was observed at chainage 2700m and 4200m surrounding the road due to lack of opening to drain out water. Temporary interruption of natural drainage and local drainage congestion may also occur during construction of drainage structures.

Mitigation:

- Two numbers of Box-Culvert at chainage 2700m and 4200m will be provided to avoid water accumulations or congestion. These will be constructed newly, where no such structures exist in the locations.
- Proper diversion structure and sufficient opening to drain out water should be developed during construction of drainage structure to avoid water congestion.

5.3 Pollution from construction materials: Dumping of construction spoils, including accidental leakage of bitumen, fuel etc. in equipment yards, is an important hazard. Both surface and groundwater might be polluted from these contaminants.

Mitigation:

- Safe transport, storage and disposal provisions for construction materials, equipment especially bitumen, fuel etc have to be carried out in order to avoid accidental spillage and loss.
- Bitumen, fuels, lubricants etc. and other hazardous materials have to be stored over raised platform not directly on the ground.
- The playground of the educational institutions shall not be allowed to use as a stack yard or work camp site.

5.4 Dust: Different construction activities, machinery movement and other works generate dust and impair the air quality. Road improvement work involves breaking up, digging, crushing, transporting and dumping of materials.

Mitigation:

- Water will be sprayed to control the dust, which is the main way to suppress dust in the working site.

5.5 **Noise:** Movement of vehicles generates noise affecting the sensitive areas. However, in this sub-project sensitive area like Primary School (2 nos.), Mosque (1 no.), Health Clinic (1 no.) etc. are likely to be affected from the road side noise.

Mitigation:

- Transportation of the construction materials have to be carried with scheduled time, mainly day time.
- All powered mechanical equipment and machinery shall be fitted with noise abating gear such as mufflers for effective sound reducing.
- A 15m long boundary wall in front of graveyard at chainage 4100m will be provided to improve road safety.

5.6 **Water Quality:** The road passes by few number of water bodies and no remarkable sources of water pollution has been found. The water quality may deteriorate if construction materials including borrow/fill materials and sand, construction waste, effluent from work camps, food waste etc. are allowed to dump in the water bodies.

Mitigation:

- Proper construction management including waste management, training of operators and other workers will be provided to avoid pollution of water bodies.
- Construction waste will be managed in specified bins opening a ditch (not in water bodies or lowland), for which contractor will be made aware.

5.7 **Occupational Safety and Sanitation:** It involves the safety problems of the construction workers and the provision for sanitation and drinking water facilities at work sites. Lack of the latter facilities might severely affect the construction workers' health condition and work efficiency.

Mitigation

- Provision for tube well to ensure potable drinking water and separate toilets for male and female to maintain proper sanitation condition will be made.
- First Aid Box with health facility at each camp site will also be made available.
- Ensure wear of proper PPE (helmet, gloves, safety glass, safety shoes etc.) of all workers during work to avoid any personal as well as construction related accident.

6. Environmental Management Plan

Specific Environmental Management Plan (EMP) has been prepared to eliminate, reduce or regulate the adverse impacts for this subproject. This EMP shall be a part of contract document.

6.1 Environmental Mitigation Plan

One of the components of Environmental Management Plan is Environmental Mitigation Plan. The environmental activities and management measures for this sub-project of RTIP-II are addressed and shown in the table below:

Sub-project Activity	Potential Environmental Impact(s)	Mitigation Measures	Estimated Mitigation Cost	Responsibility	
				Implementation	Supervision
Preconstruction					
Construction of labour camp	May occur loss of agricultural land, improper waste disposal may affect environment. Also improper sanitation facility will generate health hazard situation for the workers and the area.	Identify the location of construction camps so that minimum disturbance on agricultural land. Camps shall not be located near settlements or near water supply intakes. Place will be kept neat and clean strictly to ensure good sanitary condition. Proper toilet and water supply facilities required.	As shown in section-7	Contractor	LGED & D & SC
Removal of Vegetation	May cause soil erosion and their deposition on nearby crop field, affecting soil quality and productivity.	Vegetation will be removed from the ROW before the commencement of construction after obtaining necessary permissions	As shown in section-7	Contractor	LGED & D & SC
Setting up of Hot mix Plants and crushers	Emission of hot and polluting fumes affecting air quality, causing health hazard and damaging green habitation.	Hot mix plants, crushers and batching plants shall be located at a safe distance from the nearest habitation and dense tree area. The contractor shall obtain necessary approvals from LGED.		Contractor	LGED & D & SC
Identification of debris dumping sites	Indiscriminate dumping may cause nuisance to human habitat, cause hindrance to natural drainage of the surrounding areas.	Location of debris dumping sites shall consider the following and approved by the LGED. • Shall not be located within designated forest areas. • Dumping shall not impact natural drainage courses. Settlements are located at least 1 km away from the site.	As shown in section-7	Contractor	LGED & D & SC

Sub-project Activity	Potential Environmental Impact(s)	Mitigation Measures	Estimated Mitigation Cost	Responsibility	
				Implementation	Supervision
Construction					
Earthwork	Slope erosion, silt deposition on crop fields, dust blowing	Proper care will be taken during cutting and filling so that slope or toe of the road embankment remain within the right of way and does not damage the crop.	As described in GCC and in Section 7	Contractor	LGED & D & SC
Material sources	Improper transportation of construction materials may cause environmental pollution through dust generation and spillage	Adequate safety precautions shall be ensured during transportation of quarry material from quarries to the construction site. Vehicles transporting the material shall be covered to prevent spillage. Operations to be undertaken as per the direction and satisfaction of the LGED		Contractor	LGED & D & SC
Disposal of Debris	Improper disposal of debris may cause pollution of surrounding environment, particularly pollution of nearby water courses and hindrance to traffic.	The disposal of debris shall be carried out only at sites identified for the purpose. All arrangement for transportation during construction including provision, maintenance, dismantling and clearing debris, where necessary will be considered incidental to the work and should be planned and implemented as approved and directed by LGED.	As shown in Section 7	Contractor	LGED & D & SC

Sub-project Activity	Potential Environmental Impact(s)	Mitigation Measures	Estimated Mitigation Cost	Responsibility	
				Implementation	Supervision
Dust	Cause air pollution	• Vehicles delivering materials should be covered to reduce spills and dust blowing off the load. • In laying sub-base, water spraying is needed to aid compaction of the material. After the compaction, water spraying should be carried out at regular intervals to limit the dust to below • Plants, machinery and equipment shall be so handled (including dismantling) as to minimize generation of dust	As shown in Section 7	Contractor	LGED&D &SC
Noise	Increase of noise level of the construction site	• Noise standard at processing sites, eg. Aggregate crushing plants, batching plant, hot mix plant, any machinery will be strictly monitored to prevent exceeding of noise standards. • Workers in vicinity of loud noise, and workers working with or in crushing, compaction, concrete mixing operations shall wear	As described in GCC	Contractor	LGED&D &SC
Surface water	Contamination of surface water	• No excavation from the bund of the water bodies. • No debris disposal near any water body. • Prior written permission from authorities is required for use of water for construction activity. • Construction labours to be restricted from polluting the source or misusing the source • Labour camps will be located away from water bodies	As described in GCC	Contractor	LGED&D &SC

Sub-project Activity	Potential Environmental Impact(s)	Mitigation Measures	Estimated Mitigation Cost	Responsibility	
				Implementation	Supervision
Water Logging	During construction work or in rainy season water logging may take place	Drainage structure will be built to drain out the rain water. During construction work, diversion structure and sufficient opening should be developed to drain out water	As per BOQ of bidding document	LGED	LGED&D &SC
Construction Safety	Improper stack yard (without fence, light, signboard) may cause accident/health hazard. Improper equipment (not conforming the relevant standard) may lead to environmental pollution leakage of fuels, lubricants and emitting black smoke.	- Adequate precautions will be taken to prevent danger from electrical equipment. - No material or any of the sites will be so stacked or placed as to cause danger or inconvenience to any person or the public. - Fencing and lights shall be provided to protect the public. - All machines to be used in the construction will conform to the relevant Standards, will be free from defect, will be kept in good working order, will be regularly inspected and properly maintained as per norms and to the satisfaction of LGED.			
Health and Safety Measures	Working without health safety gear (PPE) may cause injury to the workers	- At every workplace, a readily available first aid unit including an adequate supply of sterilized dressing material and appliances will be provided as per the Labour Act-2006. - Adequate safety measures and PPE for workers during handling of materials at site will be taken up.	As described in GCC	Contractor	LGED&D &SC

Sub-project Activity	Potential Environmental Impact(s)	Mitigation Measures	Estimated Mitigation Cost	Responsibility	
				Implementation	Supervision
Operation Phase					
Traffic Movement	Road accidents may increase due to higher number of vehicles using the roads at increased speeds.	Sight views should be clear and speed breaker/rumble strip should be provided at some crowdly places. Traffic sign to be installed		LGED	LGED
	Noise levels may also marginally increase as more vehicles use the road at higher speeds	Awareness building and administrative measures should be taken		LGED	LGED

6.2 Environmental Monitoring Plan

Environmental Monitoring Plan for this sub-project will help to evaluate the extent and severity of environmental impacts against the predicted impact and the performance of environmental protection measures. The following table has been prepared for monitoring the operation & maintenance phase activities of the sub-project:

Environmental Indicator	Parameters/Units	Means of Monitoring	Frequency / Duration Standards	Responsibilities		Estimated Cost
				Implementation	Supervision	
Air Quality	Measurement PM	Inspection	Once	Contractor	D&SC & LGED	According to GCC and clause 7 of this report
Dust Control	Spraying of water	Visual	Daily	Contractor	D&SC & LGED	According to GCC and clause 7 of this report
Noise Control	Measurement db	Inspection	Once	Contractor	D&SC & LGED	According to GCC
Waste management	Monitoring of collection, transportation and disposal of solid waste. Inspection of construction camp.	Inspection	Daily	Contractor	D&SC & LGED	According to GCC and clause 7 of this report
Health and safety	Monitoring health and safety of workers	Inspection	Daily	Contractor	D&SC & LGED	According to GCC and clause 7 of this report

7 Cost of Environmental Enhancement Works and Mitigation Measures in BoQ's of Bidding Document

In consideration to the above mentioned environmental impacts and their mitigation measures for this sub-project, the following items are included in the BOQ of this sub-project.

Item No.	Description of Item	Costs (Tk)
	ENVIRONMENTAL MITIGATION & ENHANCEMENT WORKS	
1	Overall environmental management in addition to compliance to the clauses 27 & 29 of GCC to the entire satisfaction of E-I-C	
	a) Temporary camp site waste disposal facility improvement 1no@Tk.50,000.0	50,000.00
	b) Dust suppression measures[2.00 km @Tk. 2000.00/Km]	4,000.00
	c) Prevention of spillage, leakages of polluting materials	5,000.00
2	Providing and maintaining adequate potable water supply and sanitation facilities at camp site and work site to the entire satisfaction of E-I-C	
	a) Water supply: 1 no of Tube well @Tk.10,000.00	10,000.00
	b) Sanitation: 2 nos. of Toilet (1 no for women and 1 no for men) @Tk. 5000.00	10,000.00
3	Rehabilitation of ancillary sites including stockpile sites, brick crushing sites, borrow areas, workforce camp to the entire satisfaction of the Engineer in charge	30,000.00
4	Drainage facilities improvement: Two numbers of Box-Culvert would be provided.	
5	Clearing and grubbing	25500.00
6	Turfing on embankment top and slope [6785.37sqm @Tk. 15.5/sqm]	105173.2

Annex-1: Public Consultation

Public Consultations Findings for Shilmandi U.P Office (South Shilmandi)-Shilmandi Natun Bazar Road

Site: Shilmandi Bazar

Road: Shilmandi U.P Office (South Shilmandi)-Shilmandi Natun Bazar Road.

Date: 07.01. 2014

Time: 1.30 a.m. to 3.00 p.m.

Public consultation meeting were held during 1.30 a.m. to 3.00 p.m on 7th January, 2014 at Shilmandi Bazar located in the sub-project area. Md. Abdul Mojid (ARE, Narsingdi, D&SC) and Bijoy Kumar Das (Field Engineer) were present as Facilitator.

According to the participants, the road need to be improved immediately, as they are facing various problems due to the existing earthen road. Improvement of the road will provide communication facilities along with various socio-economic benefits of the area.

During discussion the environmental issues which may be affected during the road construction like, water pollution, dust pollution etc. were discussed. It was also discussed that improper disposal of construction waste will also affect the environmental quality of the area. The issue of water spraying during construction was also discussed which will reduce dust pollution. Moreover, the participants were asked to cooperate for provision of earth (less productive soil) for the construction of the road, which they agreed.

The participants requested for adopting all measures to reduce/avoid the environmental hazard during road construction.

The queries made by the participants were replied by the Facilitators Mr. Mojid properly.

The summary of the important suggestions during discussion are as follows:

- Adequate drainage facilities to be provided at all chainages to avoid water accumulations or congestion.
- Effective measure to be taken to minimize all the adverse environmental impacts of road construction works.
- Steps to be taken for minimizing the air pollution by spraying water at the construction sites.
- Noise pollution to be effectively minimized in up to a tolerable limit.

List of Participants

Sl No.	Name, Address & Telephone No.	Occupation	Signature
1	ବନାର ଗାନ୍ଧୀ ସଂସ୍କୃତିକ ସମିତି	ବ୍ୟବସାୟୀ-	ସହ
2	" ଗାନ୍ଧୀ ସଂସ୍କୃତିକ	ଅଧ୍ୟକ୍ଷ-	ମହାନ୍
3	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
4	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ	ଆୟତ୍ତି-	ଶ୍ରୀ ଶ୍ରୀ
5	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
6	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
7	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
8	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ ୦୨୨୦୭୫୫୫୫	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
9	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ-୦୨୨୦୭୫୫୫୫	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
10	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
11	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ - ୦୨୨୦୭୫୫୫୫	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
12	" ଶ୍ରୀ ଶ୍ରୀ ସଂସ୍କୃତିକ-୦୨୨୦୭୫୫୫୫	ଆୟତ୍ତି-	ନିର୍ଦ୍ଦେଶକ
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			
25			



Photograph of the Public Consultation
